SIGNAL DIRECTORATE

RESEARCH DESIGNS AND STANDARDS ORGANISATION

MANAK NAGAR, LUCKNOW - 226011

Title: Monthly Maintenance Schedule For HBL RIU - RIU (Remote Interface Unit)

SN	Issue	Version	Reason of Amendment
1	First	1.0	First Issue

Prepared by:	Approved by:
G. Pavan Kumar ED/Tele-II R N Singh ADE/Signal-5 Ashutosh Chaubey SSE/Signal	Shaminder Singh PED/QA/S&T/RDSO

Firm's Representative with	Railway Representative with
Name Designation and Date	**Name Designation and Date**

Monthly Maintenance Report — RIU

Zone	Station	RIU No	Equip No	Started	Updated
ER	Asansol	676787	77878	2026-03-30 11:07:40	2026-03-30 14:37:40

Total Points	Closed Points	Open Points
29	1	28

Module	Status
NMS	Not yet started
POWER SUPPLY	Not yet started
RIU EQUIPMENT	Open: 2, 3, 4, 5, 6, 7, 8
COMMUNICATION MODULE	Not yet started
EARTHING & SPD	Not yet started

RIU EQUIPMENT

Sl No	Description	Action Taken / Range	Observation	Remarks	Image
1	Clean the RIU Equipment and Check the communication status of the RIU COM1 & RIU COM2 Modules	To be free from dust,LEDs should be Glow/Blink PWR LED MHLT LED WHLT LED DATA1 LED DATA2 LED CH1/LINK1 LED CH2/LINK2 LED BMS LED CNS LED BHLT LED	67bjhggj	hjhj	 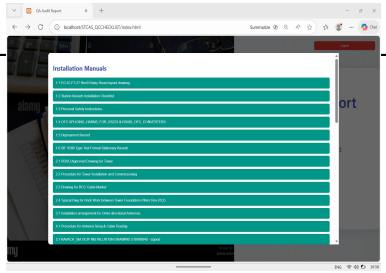
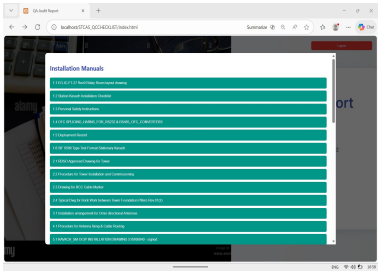
Sl No	Description	Action Taken / Range	Observation	Remarks	Image
